

RAILROAD COMMISSION OF TEXAS

WAYNE CHRISTIAN, *CHAIRMAN*
CHRISTI CRADDICK, *COMMISSIONER*
RYAN SITTON, *COMMISSIONER*

INTERNAL
OIL AND GAS DIVISION
CLAY WOODUL
ASSISTANT DIRECTOR, FIELD OPERATIONS

MEMORANDUM

May 12, 2020

MEMORANDUM TO: Chairman Wayne Christian
Commissioner Christi Craddick
Commissioner Ryan Sitton

FROM: Clay Woodul
Assistant Director, Oil and Gas Division
Field Operations


SUBJECT: Field Operations Section
Monthly Report of State Managed Well Plugging Activities
April 2020, FY 2020

Attached is the monthly report titled "State Managed Well Plugging Activities" for the Field Operations Section of the Oil and Gas Division. This report contains the following:

1. Monthly and cumulative performance measure summaries of the state managed well plugging activities of this Section.
2. Summary graphs of wells plugged, cost of wells plugged, number of salvage operations, and salvage proceeds.

The information contained in this report includes only those wells that have been physically plugged, invoiced by the plugging contractor, and approved for payment by Field Operations. Plugging operations are tracked daily to monitor the progress in meeting the FY 2020 goal of plugging 1,400 wells. As of April 30, 2020, a total of 1002 wells have been physically plugged, though not all of them have yet been invoiced and approved for payment.

KCW
Attachments


Clay Woodul
Assistant Director, Oil and Gas Division
Field Operations

cc: (via email)
Wei Wang, Executive Director
Danny Sorrells, Director, Oil & Gas Division
Megan Neal, Director, Office of General Counsel-Enforcement
Jeremy Mazur, Director Government Relations
Paul Delaney, Internal Auditor
R.J. DeSilva, Director Communications
Fisher Reynolds, Office of the Governor
District Directors

RAILROAD COMMISSION OF TEXAS
Oil and Gas Division
Field Operations Section
Monthly State Managed Plugging Activities
April 2020

Outcome Measure: Percentage of Known Orphaned Wells Plugged with the Use of State Funds (State Managed Plugging/Orphaned Wells).

April	2.43%
Fiscal Year-to-date	13.57%
Performance Measure Goal	25 %

Output Measure: Number of Orphaned Wells Plugged with the Use of State Funds.

April	150
Fiscal Year-to-date	838
Performance Measure Goal	1,400

Output Measure: Total Aggregate Plugging Depth of Wells Plugged with the Use of State Funds.

April	429,915
Fiscal Year-to-date	1,930,938
Performance Measure Goal	3,400,000

Efficiency Measure: Average Number of Days to complete a State Managed Well Plugging. From Contract Award Date

April	52
Fiscal Year-to-date	51
Performance Measure Goal	60

Explanatory Measure: Number of Orphaned Wells Approved for Plugging with the Use of State Funds.

April	59
Fiscal Year-to-date	681
Performance Measure Goal	1,000

Explanatory Measure: Number of Known Orphaned Wells in Non-compliance with the Commission's Plugging Rule.

April	6,175
Performance Measure Goal	6,000

Explanatory Measure: Number of Wells Plugged, by Operators, Without the Use of State Funds.

April	1,382
Fiscal Year-to-date	3,859
Performance Measure Goal	5,500

Explanatory measure: Percentage of Active Well Operators Who Have More Than 25% of Their Wells Inactive.

April	48%
Performance Measure Goal	41%

Explanatory measure: Numbered shut-in/inactive wells.

April	136,956
Performance Measure Goal	117,000

RAILROAD COMMISSION OF TEXAS
Oil Field Cleanup

Monthly State-Funded Plugging, Pollution Abatement and Salvage Activities
Commissioners Report
04/01/2020 to 04/30/2020

State-Funded Plugging Activities

Number of wells approved for plugging this month	59
Estimated cost of approvals	\$ 1,483,700.00
Number of wells approved for this fiscal year	681
Number of approved wells remaining to plug	1525
Estimated cost to plug remaining approvals	\$ 64,245,382.84
Number of pluggings completed this month	150
Total cost to plug wells completed this month	\$ 3,381,258.58
Number of pluggings completed this fiscal year	838
Cost of pluggings completed this fiscal year	\$ 18,069,521.07


Pollution Abatement Activities

Number of pollution abatements approved this month	4
Estimated cost of approvals	\$ 9,500.00
Number of pollution abatements approved for this fiscal year	35
Number of pollution abatements remaining	57
Estimated cost to pollution abatements remaining	\$ 1,130,560.00
Number of pollution abatements completed this month	2
Total cost of pollution abatements completed this month	\$ 4,331.05
Number of pollution abatements completed this fiscal year	25
Cost of pollution abatements completed this fiscal year	\$ 415,053.82

Salvage Activities


Number of salvage activities completed this month	20
Total proceeds received this month	\$ 28,368.30
Number of salvage activities completed this fiscal year	235
Total proceeds received this year	\$ 542,579.33

State Managed Well Plugging Program Monthly Wells Plugged April 2020

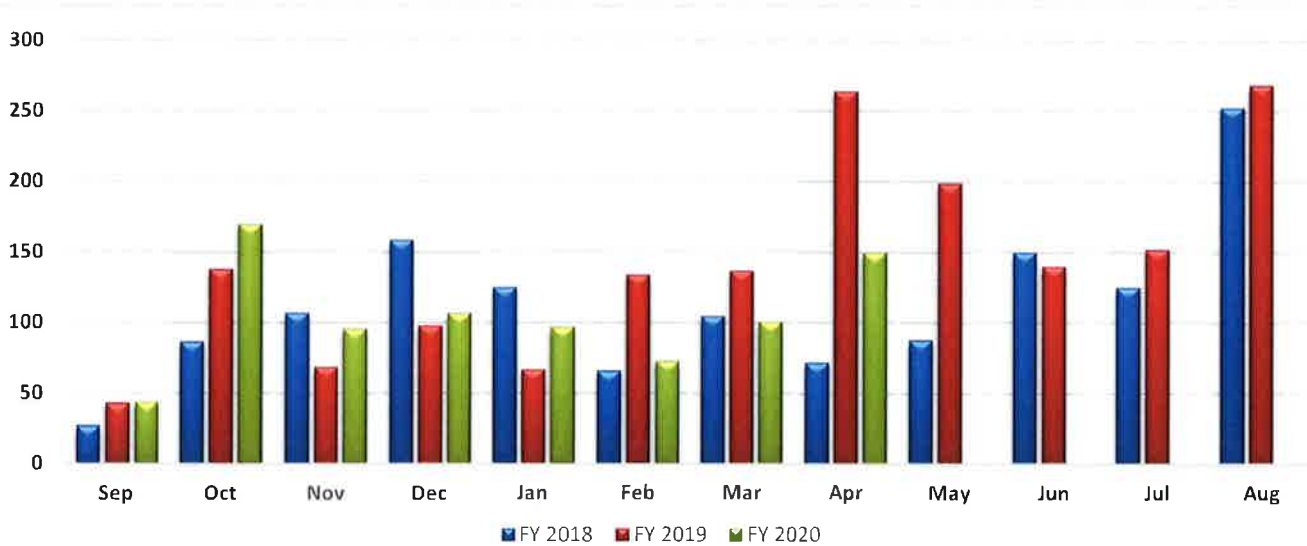


	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Tot
FY 2018	27	87	107	159	125	66	105	72	88	150	125	253	1,364
FY 2019	43	138	69	98	67	134	137	264	199	140	152	269	1,710
FY 2020	44	170	96	107	97	73	101	150					838

State Managed Well Plugging Program Monthly Cost of Wells Plugged April 2020

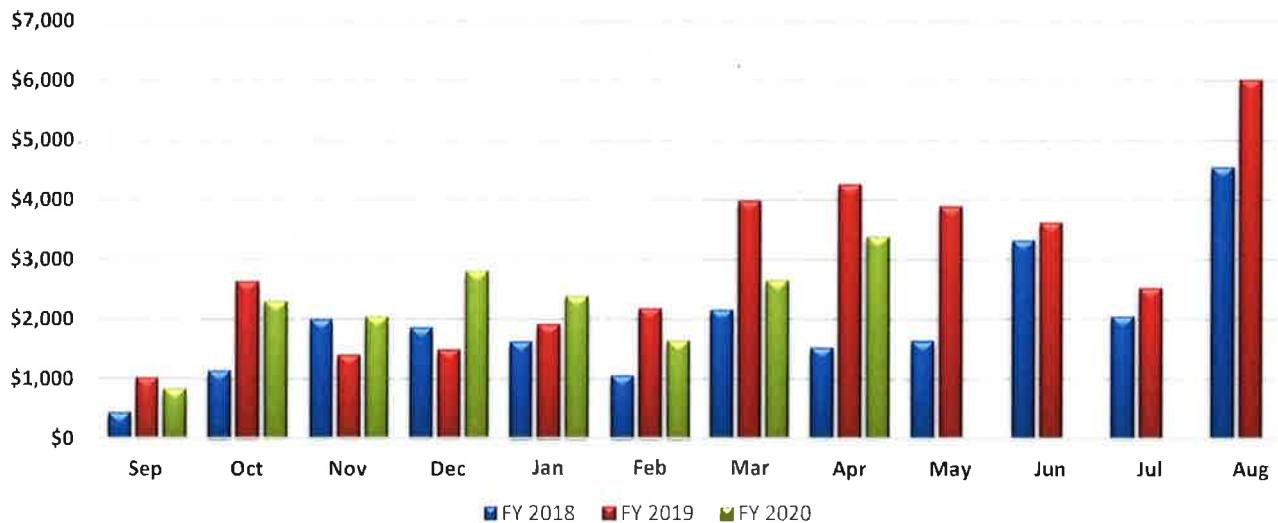


\$M	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Tot
FY 2018	\$433	\$1,144	\$1,996	\$1,865	\$1,636	\$1,064	\$2,163	\$1,532	\$1,639	\$3,319	\$2,052	\$4,550	\$23,393
FY 2019	\$1,020	\$2,637	\$1,397	\$1,494	\$1,921	\$2,181	\$3,983	\$4,257	\$3,894	\$3,617	\$2,528	\$6,014	\$34,943
FY 2020	\$831	\$2,306	\$2,044	\$2,805	\$2,395	\$1,651	\$2,655	\$3,381					\$18,069

State Managed Well Plugging Program Cumulative Wells Plugged April 2020

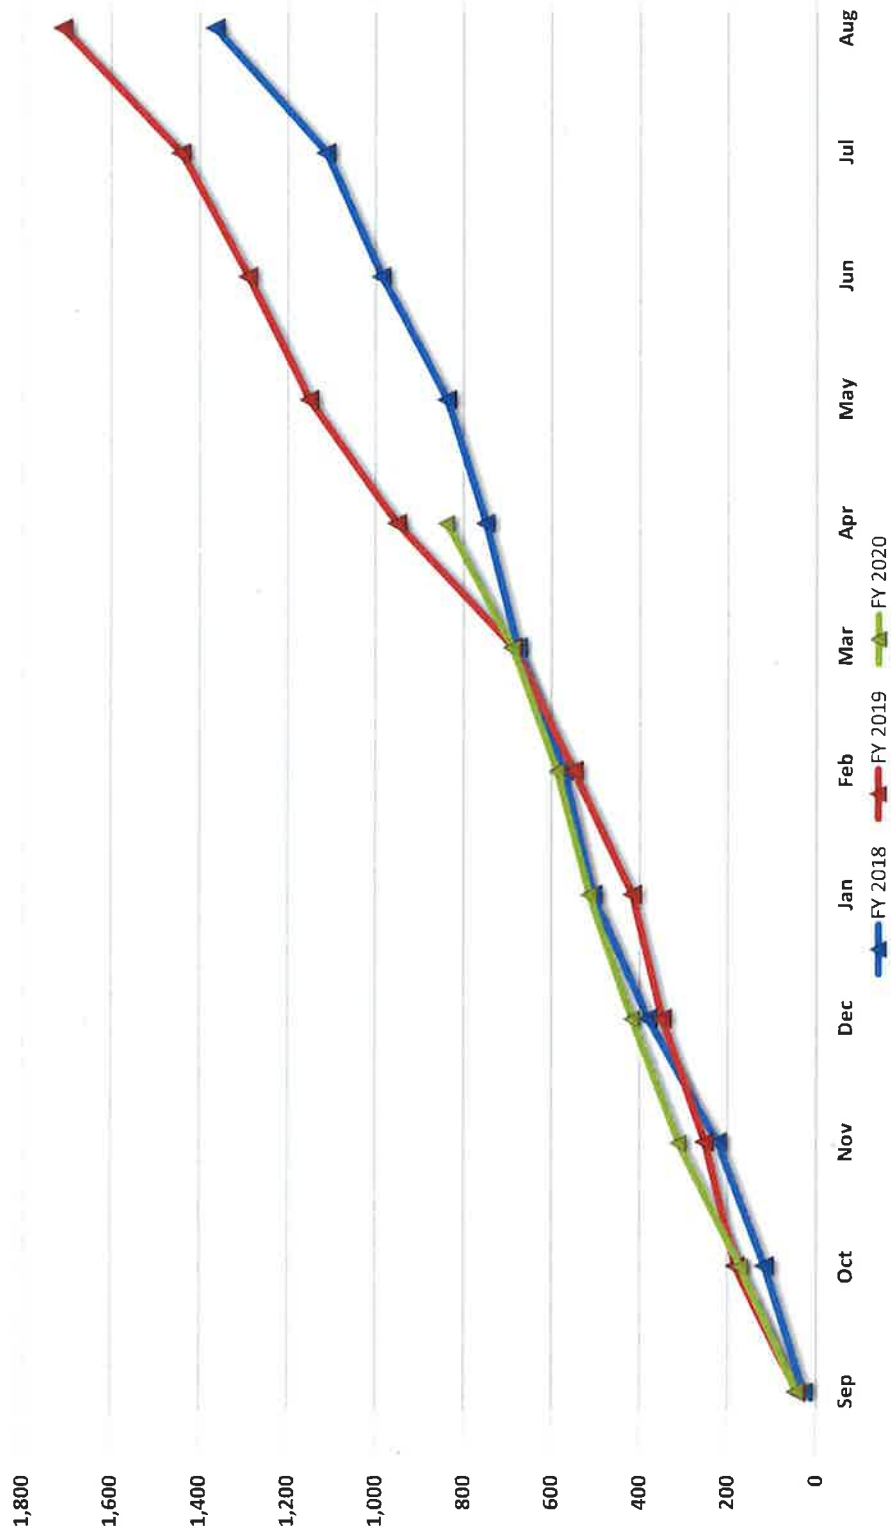


	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
FY 2018	27	114	221	380	505	571	676	748	836	986	1,111	1,364
FY 2019	43	181	250	348	415	549	686	950	1,149	1,289	1,441	1,710
FY 2020	44	170	310	417	514	587	688	838				

State Managed Well Plugging Program Monthly Salvage Operations April 2020

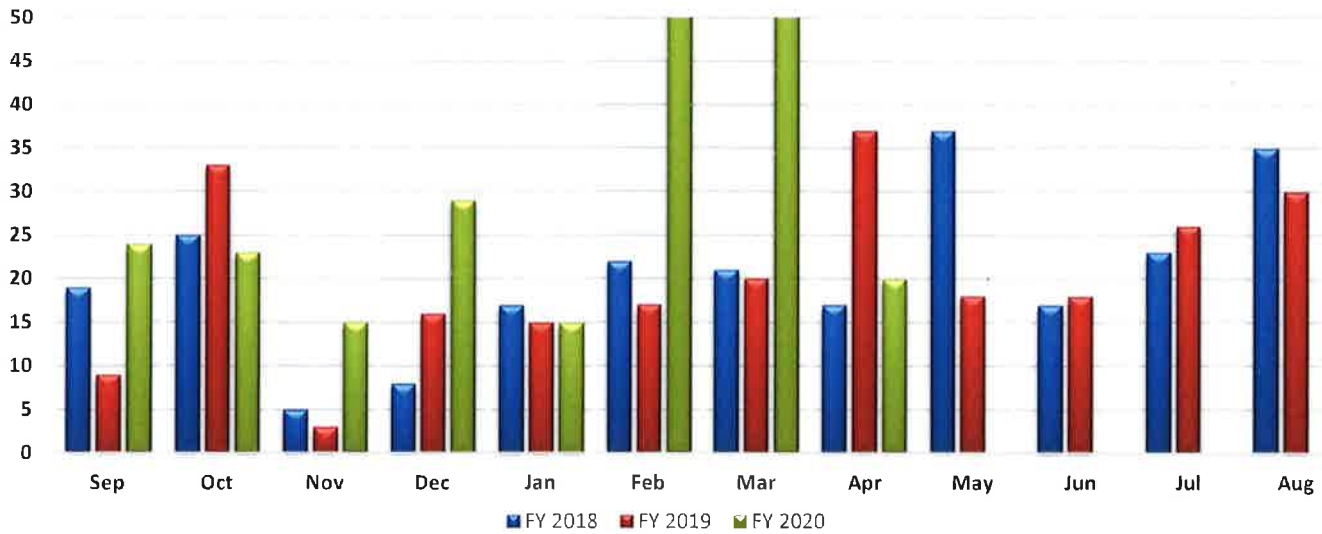


	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Tot
FY 2018	19	25	5	8	17	22	21	17	37	17	23	35	246
FY 2019	9	33	3	16	15	17	20	37	18	18	26	30	242
FY 2020	24	23	15	29	15	55	54	20					235

State Managed Well Plugging Program Monthly Salvage Proceeds April 2020

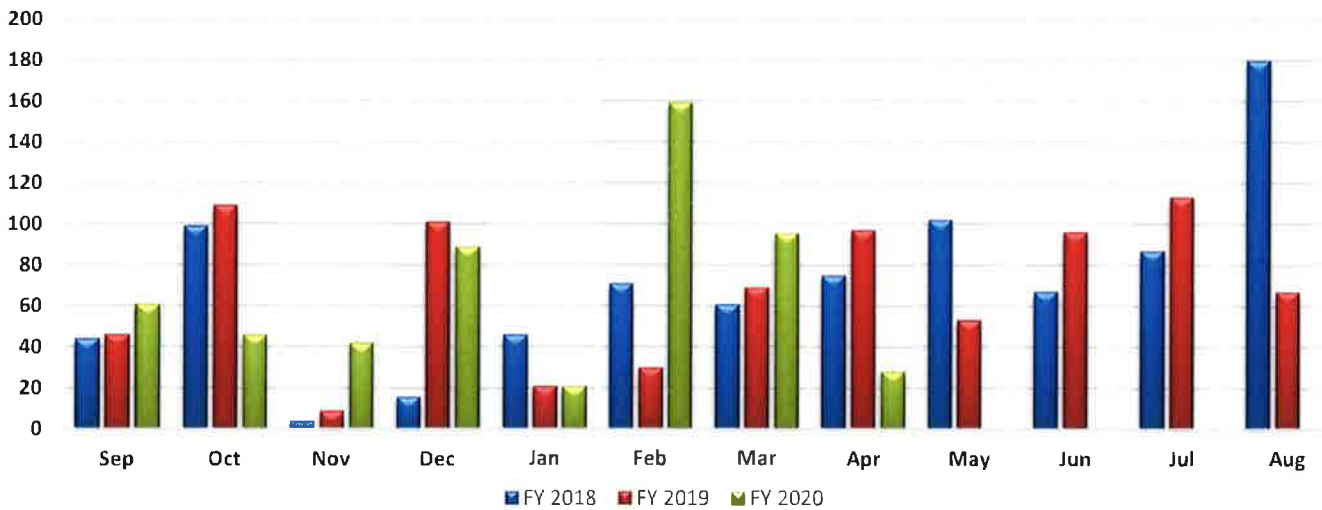

\$M	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Tot
FY 2018	\$44	\$99	\$4	\$16	\$46	\$71	\$61	\$75	\$102	\$67	\$87	\$180	\$852
FY 2019	\$46	\$109	\$9	\$101	\$21	\$30	\$69	\$97	\$53	\$96	\$113	\$67	\$811
FY 2020	\$61	\$46	\$42	\$89	\$21	\$159	\$95	\$28					\$542

State Managed Well Plugging Program Cumulative Salvage Proceeds April 2020

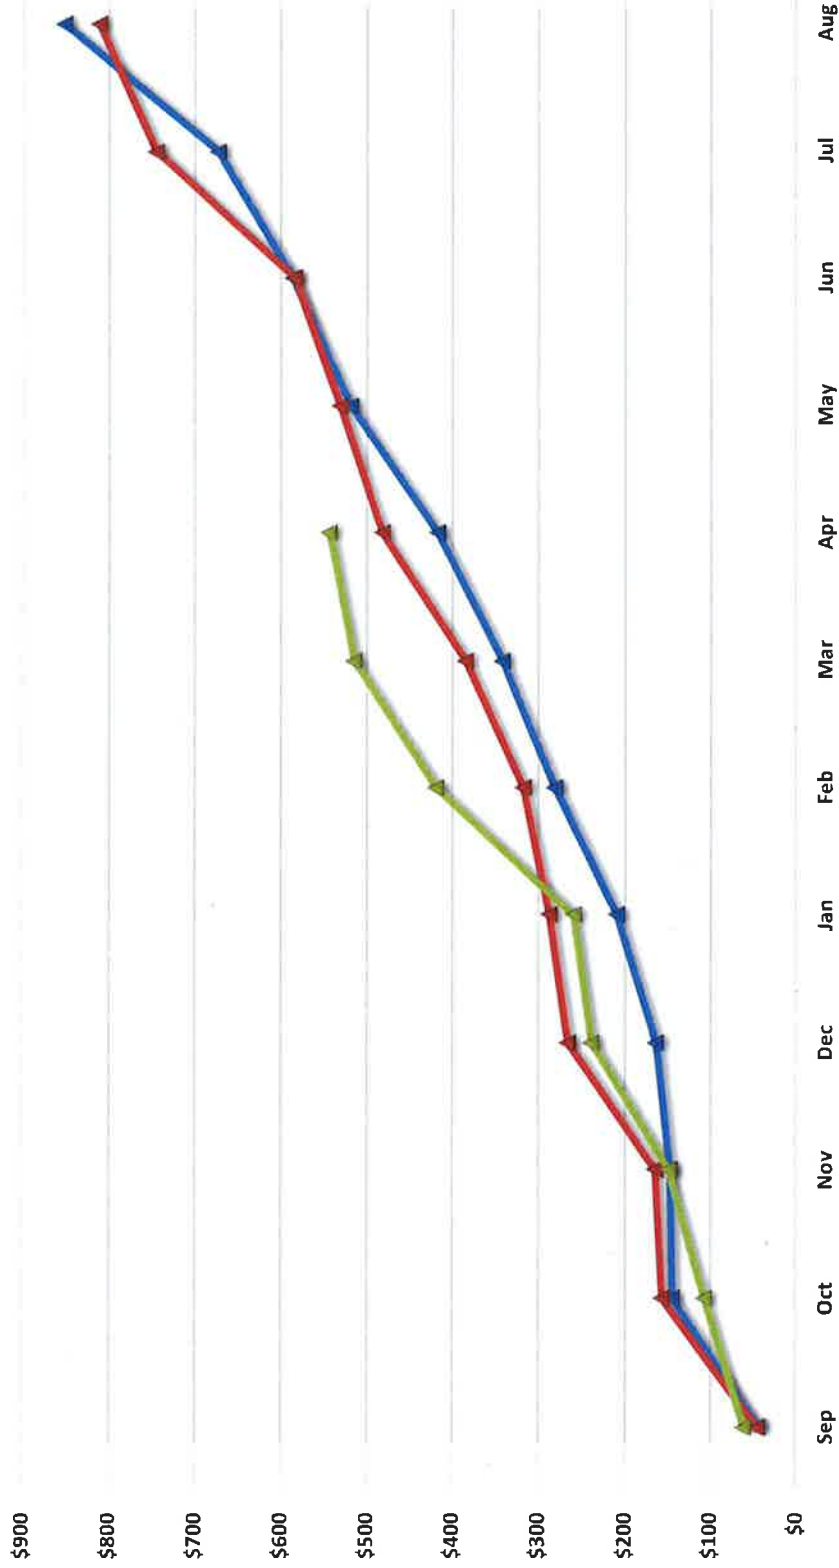

\$M	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
FY 2018	\$44	\$144	\$147	\$163	\$209	\$280	\$341	\$416	\$518	\$585	\$672	\$852
FY 2019	\$46	\$156	\$164	\$265	\$286	\$316	\$384	\$481	\$530	\$583	\$744	\$811
FY 2020	\$61	\$107	\$149	\$238	\$259	\$419	\$514	\$543				

RAILROAD COMMISSION OF TEXAS
Oil Field Cleanup
Fiscal Year State-funded Plugging Summary
08/31/2020

Run Date: May 06, 2020

Fiscal Year	Pluggings Approved	Pluggings Completed	Plugging Cost
1984	421	177	\$ 1,112,197.81
1985	474	392	\$ 2,028,121.62
1986	533	714	\$ 2,583,271.00
1987	709	703	\$ 2,106,546.67
1988	830	627	\$ 2,162,255.30
1989	844	578	\$ 2,028,764.38
1990	1004	432	\$ 1,993,128.18
1991	667	455	\$ 2,157,121.78
1992	2412	1324	\$ 5,692,878.50
1993	1171	1404	\$ 6,680,547.97
1994	1106	1325	\$ 6,003,267.26
1995	1381	1364	\$ 6,110,031.51
1996	1286	1366	\$ 5,259,382.52
1997	2156	1577	\$ 7,077,979.66
1998	1854	1604	\$ 8,456,131.53
1999	1318	1126	\$ 4,481,066.50
2000	1693	1335	\$ 5,134,842.14
2001	1612	1417	\$ 6,686,357.01
2002	1659	1464	\$ 8,011,659.30
2003	1469	1635	\$ 7,211,207.33
2004	1701	1525	\$ 7,398,237.94
2005	2168	1710	\$ 11,360,931.62
2006	1815	1824	\$ 10,736,521.32
2007	1707	1536	\$ 18,537,524.65
2008	1826	1261	\$ 14,737,537.15
2009	1557	1460	\$ 16,700,337.18
2010	1216	1181	\$ 10,504,966.23
2011	974	802	\$ 9,233,659.43
2012	755	765	\$ 12,427,517.08
2013	836	780	\$ 21,024,684.98
2014	625	564	\$ 15,069,502.11
2015	734	691	\$ 10,731,174.12
2016	810	545	\$ 8,546,936.52
2017	1104	918	\$ 11,663,682.73
2018	1979	1364	\$ 23,393,100.62
2019	1667	1710	\$ 34,942,910.72
2020	694	838	\$ 18,069,521.07
Totals	46767	40493	\$ 348,055,503.44

RAILROAD COMMISSION OF TEXAS
Oil Field Cleanup
Fiscal Year Summary for Pollution Abatements
08/31/2020

Run Date: May 06, 2020

Fiscal Year	PAs Approved	PAs Completed	PAs Cost
1984			
1985	21	14	\$ 3,563.32
1986	22	25	\$ 34,817.01
1987	42	31	\$ 25,702.15
1988	46	37	\$ 17,519.39
1989	95	72	\$ 23,521.25
1990	78	65	\$ 28,222.43
1991	146	124	\$ 72,631.81
1992	129	127	\$ 71,268.54
1993	160	124	\$ 46,586.49
1994	97	84	\$ 43,771.43
1995	86	68	\$ 29,567.34
1996	124	100	\$ 47,895.29
1997	137	73	\$ 38,268.97
1998	174	148	\$ 92,235.78
1999	136	157	\$ 70,854.70
2000	151	79	\$ 359,441.08
2001	115	61	\$ 116,091.54
2002	125	85	\$ 146,095.87
2003	117	223	\$ 161,975.21
2004	125	170	\$ 135,450.45
2005	93	121	\$ 415,879.04
2006	135	75	\$ 72,209.86
2007	83	54	\$ 546,481.92
2008	140	123	\$ 224,762.50
2009	92	58	\$ 147,553.92
2010	102	168	\$ 234,175.42
2011	58	61	\$ 123,533.00
2012	52	43	\$ 456,770.84
2013	56	57	\$ 407,575.65
2014	47	44	\$ 151,491.05
2015	51	85	\$ 231,449.74
2016	41	43	\$ 204,610.26
2017	42	42	\$ 1,274,119.25
2018	34	31	\$ 298,045.94
2019	51	28	\$ 2,107,306.18
2020	35	25	\$ 415,053.82
Totals	3238	2925	\$ 8,876,498.44
